(Unofficial Translation)

Guidelines for applying to the "Project of Decommissioning and Contaminated Water Management (Development of Analysis and Estimation Technology for Characterization of Fuel Debris (Development of Technologies for Enhanced Analysis Accuracy and Thermal Behavior Estimation of Fuel Debris))"

> Date: March 6, 2020 Management Office for the Project of Decommissioning and Contaminated Water Management

The Management Office for the Project of Decommissioning and Contaminated Water Management (hereinafter referred to as "PMO") solicits entities to implement subsidies for the "Subsidized Project of Decommissioning and Contaminated Water Management (Development of Analysis and Estimation Technology for Characterization of Fuel Debris (Development of Technologies for Enhanced Analysis Accuracy and Thermal Behavior Estimation of Fuel Debris))". Details of the project are stipulated in this Guidelines; furthermore, the procedures for implementation of the project are stipulated in the "Grant Policy for Subsidy for the Project of Decommissioning and Contaminated Water Management".

1. Purpose of Project

This project aims to support development of technologies contributing to decommissioning and contaminated water management of the Fukushima Daiichi Nuclear Power Station (hereinafter referred to as "Fukushima Daiichi NPS") of the Tokyo Electric Power Company Holdings, Incorporated (hereinafter referred to as "TEPCO") based upon the "Mid-and-Long-Term Roadmap towards the Decommissioning of Fukushima Daiichi Nuclear Power Station of Tokyo Electric Power Company Holdings, Incorporated" (hereinafter referred to as "Mid-and-Long-Term Roadmap towards the Decommissioning Research and Development Plan for FY 2020" (The 75th meeting of Secretariat of the Team for Decommissioning and Contaminated Water Countermeasures / PMO), so that the decommissioning and contaminated water management of Fukushima Daiichi NPS can be implemented smoothly, and that may lead to the improvement of Japan's science and technology standards.

Please note that this project is implemented under the engineering and project administration activities performed by TEPCO in Fukushima Daiichi NPS, and the results obtained from this project will be utilized for the engineering activities conducted by TEPCO.

2. Contents of Project

It is important to develop necessary technology to analyze and estimate the characterization of fuel

debris in order to obtain useful information for each decommissioning process (fuel debris retrieval, containing, transportation, storage, etc.). For instance, that grasping the chemical contents of nuclear fuel such as uranium and plutonium in fuel debris by clarifying chemical composition through analysis of fuel debris lead to improvement of evaluation for criticality of fuel debris.

The accident at Fukushima Daiichi NPS was the first core melting accident in the word which occurred to the boiling water reactor (hereinafter referred to as "BWR"). BWR is a reactor type having characteristics of containing large number of core internal structures such as core shrouds made of stainless steel inside the reactor pressure vessel and using boron carbide as neutron absorber. It is considered that the UO2 as nuclear fuel and fission products (hereinafter referred to as "FP") melted at a lower temperature than their normal melting points as a result of their reacting with the above-said materials whereby forming alloys and ceramics such as oxides and borides and accordingly, the fuel debris also contains such materials. In the analysis of fuel debris, for analyzing some analysis items fuel debris need to be dissolved before analysis, and in that case, it is important to completely dissolve it and make it a uniform liquid in order to improve analysis accuracy, however, fuel debris in Fukushima Daiichi NPS contains ceramics and has high chemical stability, and is often insoluble. Therefore, there is a possibility that fuel debris cannot be melted, and it is necessary to develop melting technologies.

Up to now, the following contents have been clarified in preceding subsidized project "Development of Technologies for Grasping and Analyzing Properties of Fuel Debris" (FY2017, 2018) * through analyzing very tiny amount of simulated fuel debris.

- When using acid dissolution technology, it is difficult to completely dissolve the fuel debris, and there is a high possibility that insoluble residues remain.
- When using alkali dissolution technology, it is high possibility to dissolve very tiny amount of fuel debris in Fukushima Daiichi NPS.

Therefore, in this project, the following contents shall be implemented in order to assure and further improve the analysis accuracy.

- Verification of solubility of acid dissolution technology and alkali dissolution technology for fuel debris taken by trial retrieval starting in 2021 (verification using larger simulated fuel debris than that of preceding subsidized project)
- (ii) Development of dissolution methods (review of condition such as liquid solution to dissolve, immersion temperature and time, etc.) that minimize the amount of insoluble residue generated, and methods that complement the analysis accuracy even when insoluble residue remains
- (iii) Development of methods to understand the range and causes of variation in analytical values due to differences in dissolution technology and analysis method, and to discount the range and cause of variation due to difference of methods, in order to enhance the analysis

accuracy under assumption of using multiple dissolution technologies and analytical methods for characterization of fuel debris having high uncertainty

In addition, in this project, technology to more accurately estimate the thermal behavior of fuel debris shall be developed, utilizing the test result of stopping reactor water injection at Unit 1, 2, and 3 at Fukushima Daiichi NPS by February 2020.

As this project is closely related to preceding subsidized project "Development of Analysis and Estimation Technologies for Characterization of Fuel Debris" (FY2019, 2020), information about the results, etc. of this project shall be provided to subsidized entity that has been implementing "Development of Analysis and Estimation Technologies for Characterization of Fuel Debris" (FY2019, 2020), through PMO.

* When preparing a proposal for this project, the results of "Development of Technologies for Grasping and Analyzing Properties of Fuel Debris" (FY2017, 2018) implemented in FY2018 shall be considered. Please refer to the website below. After grant decision, when the FY2019 results of preceding subsidized project "Development of Analysis and Estimation Technology for Characterization of Fuel Debris" (FY2019,2020) are made public, this project shall be implemented confirming the contents of the FY2019 results.

<FY2018 results of the project "Development of Technologies for Grasping and Analyzing Properties of Fuel Debris" (FY 2017, 2018)>

https://en.dccc-program.jp/2224 <Website of whole Project Result> https://en.dccc-program.jp/category/result

(1) Development of technologies to improve the accuracy of analysis

There are various methods to dissolve and to complement the analysis accuracy when insoluble residue remains. For instance, there could be various dissolution methods depending on the conditions such as liquid solution to dissolve, immersion temperature and time, etc.. The area of expertise in dissolution and analysis methods differ for each institution engaged in analytical works. Taking above mentioned points into consideration, in order to carry out the development of above (i) to (iii), simulant fuel debris larger than that was used in the another subsidized project "Development of Technologies for Grasping and Analyzing Properties of Fuel Debris" (FY2017, 2018)* shall be manufactured, and using larger one the simulant fuel debris analysis shall be carried out by more than one institution. Then the institutions performed the analysis, shall gather and share the results. Through these activities, measures shall be developed to reduce the amount of insoluble residue generated and complement the analysis accuracy when insoluble residue remains by sorting out the

differences in solubility due to dissolution technology. The range and cause, etc. of the variation in analytical value due to differences in dissolution technologies and analysis methods shall be clarified and a method shall be developed to handle the analytical values by discounting the range and cause of variation due to differences in methods.

In the analysis of simulant fuel debris, analysis and evaluation plan including acceptance inspection in the hot cells and dissolve process shall be drafted so that it can be applied to actual fuel debris analysis in the future. The following points (*) shall be taken into consideration when drafting and implementing the analysis and evaluation plan.

<Points to be considered in drafting the analysis and evaluation plan (*) >

• All institutions shall analyzes simulant fuel debris without information about mixing ratio of raw materials. To ensure the fairness, the institution which does not conduct the analysis in hot sell shall manufacture simulant fuel debris. The method to enable manufacturing simulant fuel debris with homogeneous composition shall be selected. Both uranium which is fuel component and zirconium which is cladding tube component shall be mixed in simulant fuel debris, and the addition of boron carbide which is a neutrons absorber and stainless steel and concrete which are elements of structure materials shall be considered in drafting the analysis and evaluation plan.

 In order to examine the process after receiving fuel debris retrieved from Fukushima Daiichi NPS, the analysis of simulant fuel debris shall be conducted in hot cells. In this analysis the emphasis shall be put on the chemical composition analysis. The detailed conditions such as analysis method, device, machinery and pretreatment process shall be investigated in drafting the analysis and evaluation plan. However, as the nuclides licensed to be used in hot cells are different in each institution, if the analysis of simulant fuel debris containing uranium in hot cells is impossible, i) the method of analysis of simulant fuel debris containing uranium and ii) the method of examining the process of trial operation before using the radioactive substance in the hot cells shall be investigated in drafting the analysis and evaluation plan.

(2) Development of technologies to estimate the thermal behavior of fuel debris

Technologies to more precisely estimate the thermal behavior of fuel debris in the PCV at the Fukushima Daiichi NPS shall be developed. For this development, it shall be firstly developed that a method for calculating and evaluating the exothermal behavior and cooling conditions simulating the PCV inside conditions for Unit No.2 reactor of Fukushima Daiichi NPS, where understanding the situation inside the PCV is the most advanced and verifying the estimation results is easier than those of others.

 In the development, the distribution of FP which is the main source of the heat generation of fuel debris, is aligned to the 3D dose distribution (*1) in PCV, which has already been formulated by Japan Atomic Energy Agency (hereinafter referred to as "JAEA".). The heat generation of fuel debris is aligned to the decay heat of inventory found in JAEA-Data/Code 2012 018 "Evaluation of Fuel Composition of Fukushima Daiichi NPS" (*2).

• As regards the distribution of fuel debris, it shall be aligned to "Estimated Diagrams of the Debris Distribution and RPV/PVC Conditions" being produced by TEPCO after being estimated by another subsidized project "Upgrading Level of Grasping State inside Reactor"(*3). However, assuming the case where evaluation of detailed distribution amount could be updated by the future interior investigation, the structure of fuel debris distribution shall be adopted so that the structure can be aligned to such updates.

 Heat radiation by natural convection shall be adopted in the evaluation system, because natural convection associated with heat generation is considered to be occurring inside the PCV.

• If any data is unavailable such as the correlation between porosity and thermal properties, the data shall be obtained by conducting measurements in which the level of porosity of materials is gradually altered. Based on the measured data, the correlation between porosity and thermal properties shall be calculated and applied to the evaluation.

• In order to verify the appropriateness of the case to which each of the above-said conditions is applied, the past temperature history shall be reproduced by collating the temperature data and water injection data (*4) of Unit 2 Reactor, which have been recorded for nine years continuously after the accident. After the past temperature history is reproduced, temperature distribution of air-cooling conditions, temperatures of fuel debris under air-cooling conditions, etc. shall be examined on the assumption that the volume of water injection is zero.

Since there are many detailed items need to be considered on implementation in the above (1), after completing drafting the plan, under PMO's coordination close examinations on the contents of the drafted plan are conducted by related organizations (METI, TEPCO) and Nuclear Damage Compensation and Decommissioning Facilitation Corporation (NDF) before proceeding to the next step. In consideration of the latest on-site information and internal investigation results, etc., the experimental retrieval device of fuel debris and the first retrieval of fuel debris are to be implemented under coordination with another subsidized project "Development of technology for fuel debris retrieval gradually expanding its scale" and sufficient coordination and cooperation with related organizations.

*1 K. Okumura, et al., Technology Development to Evaluate Dose Rate Distribution and to Search for Fuel Debris Submerged in Water for Decommissioning of Fukushima Daiichi Nuclear Power Station (8) A prediction of the three-dimensional dose rate distribution in the primary containment vessel, 2018 Autumn Meeting of the Atomic Energy Society of Japan, 3A01

 $\mathbf{5}$

*2 K. Nishihara, et al., Estimation of fuel compositions in Fukushima-Daiichi Nuclear Power Plant, JAEA-Data/Code 2012-018, Japan Atomic Energy Agency <u>https://jopss.jaea.go.jp/search/servlet/search?5036485</u> [Japanese text only]

*3 The summary results on subsidy program for the" Project of Decommissioning and Contaminated Water Management (Upgrading Level of Grasping State inside Reactor"(FY 2016,2017) implemented in the FY2017

https://en.dccc-program.jp/786

*4 Parameters related to Fukushima Daiichi Nuclear Power Station on the TEPCO's website <u>http://www.tepco.co.jp/decommission/data/plant_data/</u> [Japanese text only]

3. Operation of research and development

(1) Gathering domestic and overseas wisdom

Projects must be conducted by utilizing domestic and overseas wisdom. In particular, they must consider mobilizing necessary technologies and knowledge both from Japan and overseas broadly. In case of development of machines and equipment, establishment of common basis of the machines and equipment (utilization of widely used goods and goods which have already been developed, etc.) must be taken into account as much as possible in order to promote reasonable development. Furthermore, in the development of evaluation method, it is important to be validated and reviewed objectively by third parties such as academic societies, etc. Hence, such validation and review must distinctively be placed in the development plan or be set as a milestone.

In implementing the project by introducing domestic and foreign technologies and knowledge, if necessary, the external organization shall be chosen through a public bid such as a general competitive bidding in a timely manner; and in order to ensure transparency and fulfill accountability, the information on the public bid must be published on the website and the link to the information must appear the PMO's webpage, with the intention to disseminate it widely.

(2) Establishing Decommissioning Industrial Cluster to Fukushima and Innovation Coast Framework Realization

It shall be considered to work with companies, which run business in Hamadori area and other region*, in an aim to promote local companies engaged in decommissioning related industry and establish decommissioning industrial cluster to Fukushima.

It shall be also considered to use decommissioning related facilities (e.g. Naraha Center for Remote Control Technology Development (mock-up testing facility), Okuma Analysis and Research Center (Laboratory for analysis and research of radioactive substances), which play

a role in Fukushima Innovation Coast Framework.

*Area

Iwaki city, Soma city, Tamura city, Minami Soma city, Kawamata town, Hirono town, Naraha town, Tomioka town, Kawauchi village, Okuma town, Futaba town, Namie town, Katsurao village, Shinchi town, litate village

(3) Human resource development for medium and long-term

Efforts need to be made to strengthen the relationship with universities, research organizations, etc. through implementing joint research, etc. from the viewpoint of human resource development in the middle and long-term.

(4) Clarification of tests conditions and specifications for development

Consideration of requirement level necessary for implementing decommissioning activities must be done before commencement of elements tests and equipment design; furthermore, evaluation of to what extent existing technologies can be utilized must be done as quantitatively as possible. Based upon these, information on the target of the degree of the tests and equipment development compared to the requirement level must be shared with concerned parties, and the test conditions and design specifications must be established.

(5) Definition of criterion for judgment of degree of objective achievement

Comprehensible criteria which can be a measure for the judgment of objective achievement of the project must be defined using numerical values, etc. (Refer to Table 1); and they must be validated whether or not the objective will have been achieved at the completion of the project.

	Table T Definition of Technology Readiness Level (TRL)			
Level	Definition corresponding to this project Phase			
7	At the stage of completion of practical utilization	Practical use		
6	At the stage of being demonstrated in the field Field demonstration			
5	At the stage of production of prototype with the scale of practical use, and demonstration in a simulated environment such as in a factory, etc.	Demonstration of simulation		
4	At the stage of implementation of function tests at the level of trial production as a process of development and engineering	Research for practical use		
3	At the stage of proceeding with development or engineering using application or combination of existing experiences. Or at the stage of proceeding with development or engineering based upon elementary data in the area with lack of existing experiences.	Application research		

Table 1 Definition of Technology Readiness Level (TRL)

2	At the stage of proceeding with development or engineering in the area nearly without applicable existing experiences, and with setting up the specifications.	Application research
1	At the stage of clarifying elementary contents regarding development or engineering.	Elementary research

(6) Cooperation with decommissioning activities and associated research and development projects

Clarify how the results obtained could contribute to the decommissioning activities and associated research and development projects, and positive cooperation and collaboration with the associated research & development projects shall be conducted. For this purpose, it is necessary to share harmonized input /output information among the associated research and development projects. In order to realize this information sharing, coordination among the entities involved must be done using Form 4 at the commencement of the project and other suitable timings; and it must also be regularly shared with and confirmed by PMO and other concerned entities. Furthermore, the information on implementation of the project (such as progress situation, acquired data, challenges, etc.) must be shared with and offered to PMO and the concerned entities in a timely and appropriate manner. Also, Non-Disclosure Agreement must be concluded among the Subsidized Project Operating Entities, the associated research & development project entities and PMO, if necessary. PMO will conduct the necessary coordination.

(7) Research management

The project must be proceeded with bearing in mind that the achievement goals of the project (such as the contents of outputs, target schedule, etc.) were established so as to achieve high-rank goals of this project.

Furthermore, it is necessary to create a flexible implementation organization that can reflect the following matters to the project, because understanding about the situation of the inside of PCV and necessary R&D to retrieve fuel debris is still limited, and a great deal of uncertainties remain in respect of the preconditions for research development.

- [1] Discussions about the Mid-and-Long-Term Roadmap, discussions at meetings of the Secretariat of the Team for Decommissioning and Contaminated Water Countermeasures, and instructions and advices given by the Agency for Natural Resources and Energy, and so forth.
- [2] Discussions concerning the "Technical Strategic Plan for Decommissioning of the Fukushima Daiichi Nuclear Power Station of Tokyo Electric Power Company Holdings, Inc.", discussions at meetings held by and instructions and advice given by Nuclear Damage Compensation and Decommissioning Facilitation Corporation, and so forth.
- [3] Progress management, instructions and advices given by PMO in which Nuclear Damage Compensation and Decommissioning Facilitation Corporation have joined.

In particular, in order to achieve the project outcome targets, it is important to promptly understand and reflect the current status of Fukushima Daiichi NPS, the progress of TEPCO's engineering, internal investigation, R&D, on-site working environment improvement such as dose reduction, lowering water level, space availability, etc. It is also important to check whether the prerequisites of the project are satisfied not only at the early stage of the project but also at any time to during the project from the viewpoint of on-site applicability, and to take measures promptly if any issues are found.

Therefore, under the project management of TEPCO, it is required to establish organization to conduct R&D. When grant application, application shall be made jointly with TEPCO. However, TEPCO does not claim for any expenses for this project. When working at Fukushima Daiichi NPS, etc. for on-site investigation and demonstration test and so on, sufficient coordination shall be made beforehand with TEPCO, management system shall be constructed with understanding the compliance issues and precautions, etc., and appropriate security measures shall be taken.

(8) Progress report

The entity is required to report implementation plan, progress situation, project results, etc. to PMO on request. Especially, the implementation situation must be reported at the end of every month by using the implementation schedule as described in Reference Document 2, etc., and at the time when PMO request, and after completion of the project, results report must be established and submitted.

Please be noticed that PMO is entitled to share the submitted information with the concerned organizations on the basis of "5. Implementing Scheme" with due considerations to the nondisclosure information stipulated by Act on Access to Information Held by Administrative Organs (Act No. 42 of May 14, 1999).

(9) Enhancement of outreach

Comprehensible explanation to the public regarding the project contents and results is indispensable. The entity is also required to actively cooperate with the government and the concerned organizations for dissemination of information. In addition, any results of the project, which could be made public, should be disclosed as soon as possible after its completion.


(10) Preparation of other options

Alternative options must be prepared for the case that the project cannot be proceeded with as planned during the project term. If the alternative options are prepared or revised, the information must be notified to PMO.

4. Project Term

From the effective day (of the grant) to March 31, 2021

5. Implementing Scheme

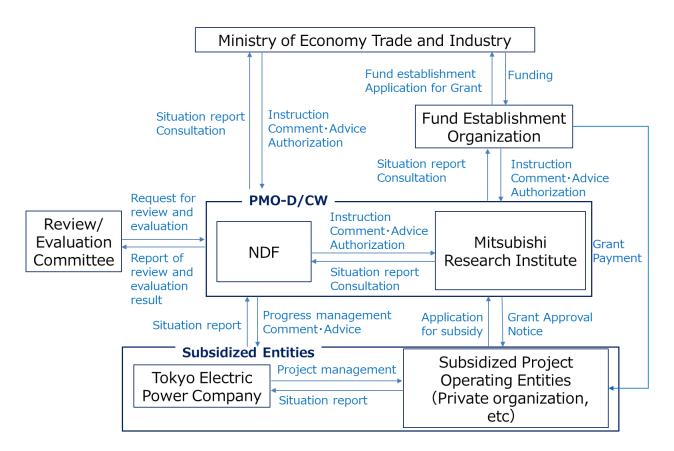

6. Application Requirements

The private companies, etc. satisfying all of requirements (1) to (9) shown below are qualified to apply for the subsidies. Applications from consortia are also acceptable. In that case, a managing legal entity must be appointed out of each consortium and submit the project proposal. (Please note that no managing legal entity may commission the entire work to another legal entity.)

- (1) Possessing the organization for properly conducting the relevant subsidized project.
- (2) Having the capacity, knowledge and experience required for conducting the relevant subsidized project.
- (3) Having the management foundation required for smoothly conducting the relevant subsidized project and sufficient ability to control the funds and other resources.
- (4) Being able to follow the appropriate accounting procedures in accordance with the "Grant Policy for Subsidy for the Project of Decommissioning and Contaminated Water Management" and the "Subsidized Project Administration Manual (*)". With regard to overseas entities, as a general rule, being able to prepare the evidenced documents in Japanese or English, and present them in Japanese territory on demand from the PMO.

(*)https://en.dccc-program.jp/files/20200306man.pdf

(5) Not foreseen to be subject to Articles 70 and 71 of the Cabinet Order concerning the Budget,

Auditing and Accounting.

- (6) Not fulfilling any of the conditions stipulated in the "Guidelines for the suspension of subsidies controlled by the Ministry of Economy, Trade and Industry and the suspension of designation relating to the contracts". (January 29, 2003, No 1) First column, the second items in Attachment
- (7) The applicant must have a compliance system under a self-regulated structure which meets the "Standards for Exporters, etc. to Meet" provided for in Article 55-10 (1) of the Foreign Exchange and Foreign Trade Act. We will confirm this system using (Form 3) "Response to Security Export Controls" when selecting applicants, so please use this form to fill in the required items and submit the required documents.

[Reference] Standards for Exporters, etc. to Meet

Regulations to be observed by parties engaged in export or provision of technology in the course of trade (exporters).

Exporters that do not handle security-sensitive "specified important goods, etc." have a duty to 1) nominate a person responsible for checking goods, etc., and 2) provide guidance to managers and export workers on compliance. Exporters that do handle security-sensitive "specified important goods, etc." have a duty to 1) identify a representative as the responsible person, 2) set out an export control system, 3) set out a procedure for checking regulated/non-regulated goods, 4) set out a procedure for confirming the usage and consumer, and confirm these in accordance with that procedure, and 5) confirm that the goods to be shipped coincide with the confirmed non-regulated goods at the time of shipping.

- (8) Admitting that the results obtained through this project can be utilized by TEPCO, etc. to leverage them for Decommissioning and Contaminated Water Countermeasures if they request to do so under the condition that each party is in agreement. Not preventing the utilization by behaviors such as not allowing to use the technology intentionally, asking for unreasonable compensation, etc. in spite of receiving the request.
- (9) In order to make sure of the above-mentioned item, preventing a situation where the results from this project are not be able to be utilized for Decommissioning and Contaminated Water Management Countermeasures at the Fukushima Daiichi NPS by ceding the above-mentioned condition in (8) to the successor if the applicant transfers the result to a third party and loses their own right to utilize it accordingly. In the case of a conflict which makes the applicant unable to make sure of the items in (8), the concerned parties must solve it by their own responsibility.

7. Requirement Conditions for Grant Decision

- (1) Number of proposals to be adopted : One proposal or more
- (2) Subsidy rate and maximum amount of subsidy
 - The subsidy is fixed in JPY.

Maximum amount: 200,000,000 JPY

Subsidies are paid in JPY. The contents of the project, amount of the subsidy, etc. will ultimately

be settled only after coordination with PMO.

(3) Time of Payment

In principle, the subsidies are paid after the project is completed.

*Please note that cases where the payment (i.e. the payment by estimate) before the completion of the project is permitted are limited.

(4) Confirmation of the amount of payment

The amount to be paid is decided based on the Project Result Report which is submitted by the operating entities after the project is complete as well as the results of the survey at the verification site and/or the office.

The amount to be paid will be the total of the expenses to be covered by the subsidies, which do not exceed the granted subsidy amount. For this reason, the account ledgers, receipts and other documents are necessary for supporting all the expenses. All the expenses will be strictly inspected and evaluated. Thus, the expenses not meeting the conditions mentioned above may be rejected.

(5) Grasp the implementation organization at the time of submitting the Project Result Report

Since the Ministry find necessary to confirm the implementation organization of the project, when submitting the Project Result Report after the project is completed, as expenses are covered by the subsidy in the case of outsourcing or commissioning contract, the Subsidized Entity must attach the implementation organization document (*) describing the name of the contractors (only for transactions of 1 million yen or more including tax), their relationship with the Subsidized Entity, their address, the contract amount and the contract content.

(*) This document is to be confirmed at the inspection.

Although "outsourcing expenses" and "commission expenses" are subject to subsidy, "travel expenses", "meeting expenses", "gratuities", "equipment expenses (including rent and hire fees)", "assistant personnel costs (including temporary staffing)" are not eligible.

In the case of subcontracting or recommissioning from the contractors (in the case of subcontracting etc., limited to transactions of 1 million yen or more including tax), please describe their information in the implementation organization document same as above (There is no need to describe the contract amount for sub-subcontracting or re-recommissioning).

[Implementation Organization Document Description Template]


In principle, the implementation organization should be presented in the Organization Table as shown below and include the implementation organization chart. There is no prescribed form if the implementation organization, the name of the contractors, their relationship with the Subsidized Entity, their address, the contract amount, and the contract content are clearly stated on the document.

Implementation Organization Table (limited to contract of work/service agreement of 1 million yen or more including tax)

Name of Outsourcing/Commissionin g Company	Relationship with Subsized Entity	Address	Contract amount (with tax)	Contract content
Laboratory A, Inc.	Contractor	XXX-ku, TokyoXXX	*Using Arabic numerals, show amounts in yen value	*Fill in as detail as possible
Research Institute B, Inc.	Subcontractor (Subcontractor of Laboratory A, Inc.)	Refer to the sample above	Refer to the sample above	Refer to the sample above
Consulting C, Inc.	Subcontractor (Subcontractor of Laboratory A, Inc.)	Refer to the sample above	Refer to the sample above	Refer to the sample above
Company D, Ltd.	Sub-subcontractor (Subcontractor of Research Institute B, Inc.)	Refer to the sample above	No need to fill in (*)	Refer to the sample above
Center E, Inc.	Contractor	XXX-ku, TokyoXXX	*Using Arabic numerals, show amounts in yen value	*Fill in as detail as possible

(*) Company D, Ltd. Is a sub subcontractor from the standpoint of the Subsidized Company so there is no need to write the contranct amount.

Implementation Organization Chart (limited to contract of work/service agreement of 1 million yen or more including tax)

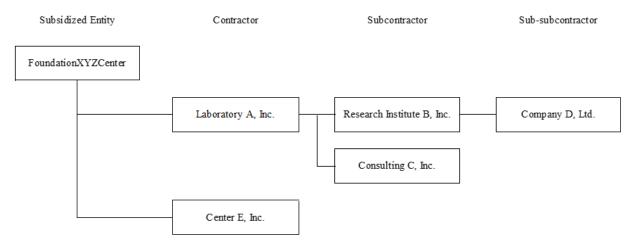

8. Application Procedure

(1) Application Period

Commencement: Friday, March 6, 2020

Deadline: By 10:00 AM local time on Thursday, March 19, 2020

We will not accept any proposals after this deadline.

(2) Information Session

Date and Time: Thursday, March 12, 2020 14:30 – 15:00

Venue: Conference Room at Mitsubishi Research Institute, Inc.

Map: https://www.mri.co.jp/en/about-us/locations/index.html

If you would like to attend the session, please inform the contact point written in "13. Contact"

by 12:00 AM on Wednesday, March 11, 2020 via email. The session will be held in Japanese. If you need a translator, please make arrangements on your own (You are responsible for the expense). If you need an information session in English, please consult with PMO by the above deadline via email. Please note that the capacity of the venue is limited.

When making contact, please title your e-mail "Register for attendance to the information session for 'Project of Decommissioning and Contaminated Water Management'" and include the "corporate or organization name," "name of the attendee," "department," "phone number," "fax number," "e-mail address," and "subsidized project name to apply" in the main text.

To applicants from the EEA member states:

Private information will be used only in the working related to explanation meetings and will not be distributed to any other organizations. When you have provided us with such information, we assume that we have received it with your clear understanding that you submit it in agreement to the above-said condition.

(3) Application form and other documents to be submitted

[1] Please submit the following documents as one file. Please title your file "Application for the subsidy program 'Project of Decommissioning and Contaminated Water Management (Development of Analysis and Estimation Technology for Characterization of Fuel Debris (Development of Technologies for Enhanced Analysis Accuracy and Thermal Behavior Estimation of Fuel Debris))'.

- Application form (Form 1)
- Outline of Subsidized Project (Form 2)
- Certificate of Conformance (Form 3)
- Input/ Output information (Form 4)
- Response to Security Export Controls (Form 5)
- Personal Data Processing Consent Form (Form 6)
- Other documents
 - Outline of Corporation or Organization (such as a brochure, etc.)
 - The financial results, and statement of revenues and expenses (of the last year)
 - The articles of association or the act of endowment
 - Other supporting documents
 - * You must submit 1 copy of the application documents using A4 paper. You can describe them in Japanese or English. If you bring the application documents with you or submit them by mail, one CD-ROM must be submitted along with the hard copies. Furthermore, submission to attach 1 copy via email to the email address for application is permitted. As a general rule, the file format must be Ichitaro, MS-Word, MS-PowerPoint or MS-Excel. If you have unavoidable reasons not to be able to use these formats, please contact us.

* If your proposal is adopted, there is a possibility that Input/Output information will be released to other entities.

[2] All the application documents submitted will not be used for any purposes other than the evaluation in the course of the selection process. Please note that the application documents submitted will not be returned. We take the utmost care to preserve confidentiality. However, if your proposal is adopted, the information except the non-disclosure information (i.e. the personal information, the information detrimental to the legitimate interests of legal entities) may be disclosed under the "Act on Access to Information held by Administrative Organs" (Act No. 42 enacted on May 14, 1999).

To applicants from the EEA member states:

Private information included in application documents will be used only in the evaluation. Therefore, PMO will not distribute such private information to any other organizations besides METI, Fund establishment organization, NDF, and Review/Evaluation committee. When you apply for the subsidy program, you must clearly understand the above-said condition and submit Form 6.

- [3] The costs spent for issuing the application documents and other documents will not be included in the expenses. Also, the costs spent for issuing those documents will not be compensated for regardless of whether the proposal is adopted or not.
- [4] The matters described in your proposal are considered to be the fundamental policies which should be observed during the project. Consequently, please be sure to describe only the matters which are feasible within the budget. Also, please note that even if your proposal is adopted, it may be rejected later on if you make a significant change to it at your discretion.
- [5] Appropriateness of the costs breakdown must be shown using supplemental explanation documents.

(4) Place of submission

The application documents must be delivered to the following address via hand-carry, mail or email, etc.

Toranomon Toyo Bldg. 8th Floor 4-2, Toranomon 1-chome, Minato-ku, Tokyo 105-0001, JAPAN Contact: Mr. Kondo, Mr. Kawai Email address for submission: hr-apply@mri.co.jp * Please DO NOT send the application documents via fax. Incomplete documents will be

rejected and not subject to evaluation. Therefore, please carefully read and follow the

procedures for application to correctly fill out the documents.

* Any application documents submitted after the closing date will not be accepted. If you send the documents by postal mail, they may not be delivered by the designated time on the closing date. Consequently, you are advised to mail them sufficiently ahead of the closing date.

9. Evaluation and Adoption

(1) Method of Evaluation

Applications will firstly be evaluated through paper screening, so that the applicants for the presentation to the review committee can be selected. This committee will be held in late March 2020. Depending on the capacity of the venue, the number of the participants to the presentation may be restricted. Furthermore, hearings and on-site investigation may be conducted as required; and submission of additional documents may be requested.

(2) Evaluation Criteria

Applications are to be comprehensively evaluated based upon the following criteria. However, the applications which have been judged not to meet the criterion [3] and [5] shall be disqualified regardless of evaluation of the other criteria.

[1] Objective, contents, implementation method, and applicability to countermeasures for decommissioning (Including adaptability to the work site)

Whether or not the Project purpose corresponds to the project purpose described in the "Guidelines for applying" is to be evaluated.

Judgment is made as to whether the contents of the project conform to the project objective and are provided specifically taking into account the applicability to countermeasures for decommissioning (including adaptability to the work site).

Whether the implementation method of the project is consistent with the purpose and details of the project is to be evaluated.

[2] Project Implementation Schedule

Whether or not the project implementation plan (timeline) is appropriate to the purpose and details of the project, etc. is to be evaluated.

[3] Project Implementation Organization

Judgement is made as to whether the entity has the project implementation structure, expertise as an organization, expertise of those who are to be engaged in the project, the track records of similar projects, and the contribution(s) to local industrial development such as working with companies which run business in the Hamadori and other regions*. We focus on whether a project implementation organization including the project leader is clearly identified, and whether it has the implementation ability and the coordination system to consider/judge the applicability to countermeasures for decommissioning (Including adaptability to the work site).

*Area:

Iwaki city, Soma city, Tamura city, Minami Soma city, Kawamata town, Hirono town, Naraha town, Tomioka town, Kawauchi village, Okuma town, Futaba town, Namie town, Katsurao village, Shinchi town, litate village

[4] Project Cost

Whether or not project costs are appropriately allocated to the project purpose and contents, etc. is to be evaluated.

[5] Financial Basis and Management System for Implementation of Project

Whether or not the applicant organization has a financial basis and a management system enabling them to implement the project is to be evaluated.

(3) Decision and Announcement of Results

PMO will release the adopted entities on our website, etc. The adopted entities will be notified of the result.

10. Grant Decision

The project shall be initiated after the adopted entity submits a grant application for the subsidy to PMO and PMO has sent a notice of grant decision in return.

It should be noted that there may be changes in the details, composition and scale of the project as well as its budget between the decision of adoption and grant, as a result of consultation with the PMO. Also, please be aware that the grant decision may not be notified if the adopting requirements are not met.

Although subsidized project operating entities may be provided with information required to implement the project after the decision of grant, they may be requested to observe the confidentiality depending on the nature of the information.

Information on the decision of grant of the subsidy (adopted date, the entity adopted (granted), effective date of the grant, corporation number in Japan, value of grant, etc.) will be shown on the Corporation Information* in principle.

* The Corporation Information operated by Ministry of Economy, Trade and Industry is a system, with the start of the 'My Number' system considered, to link a corporation number in Japan to corporation information such as those regarding subsidy and prize-giving. Anybody can execute batch retrieval/browsing in the system. With this system, expansion of new businesses, reduced costs in information acquisition, and more efficient businesses are expected in business enterprises and public offices.

Web address: http://hojin-info.go.jp (Japanese only)

11. Allocation of Expenses

(1) Classification of Expenses Covered by Subsidy

The expenses covered by the subsidy shall be those directly required for the implementation of the project and those required for compiling the project results. The specific items are listed below.

Items of Expense	Description		
(1) Labor Costs Expenses for personnel required to implement the subsidized project.			
	Expenses for raw materials, consumables, design/fabrication/processing,		
(2) Operating Costs	facility/equipment, goods purchase, research, outsourcing, travel,		
	remunerations, rent/depreciation and other necessities.		

- (2) Expenses not to be Included in Expenses Covered by Subsidy
 - Office supply equipment (furniture such as desks, chairs and bookshelves, office machinery and so forth) with which the applicants should already be provided when considering the nature of the project.
 - Expenses for handling accidents and disasters that occurred during the project. (However, cancellation fees incurred by reasons not attributable to subsidized project operating entities may be directly included as an expense. Please consult the person in charge on this matter.)
 - Expenses unrelated to the project
- (3) Exclusion of Consumption Tax from Expenses Covered by Subsidy

If general and local consumption taxes (hereinafter referred to as "consumption tax") are included in the subsidy amount, the applicants shall be requested to submit a report after the settlement of tax amount, according to the granting guidelines.

This is so specified as to demand, at the time of filing an income tax return, that subsidized project operating entities should report and return the amount to which the subsidy has been applied, out of the amount of deduction for taxable purchase, so that the amount for which the subsidy has been allocated out of the amount of deduction for taxable purchase shall not be detained.

However, because the report mentioned above is based on an income tax return that will be filed after the settlement of the subsidy, occasional delinquency in reporting due to lapse of memory has been found. Also, in order to avoid the complicated office procedures that need to be followed by subsidized project operating entities, the consumption tax shall be handled as follows.

When determining the amount of subsidy applied for in the grant application, the consumption tax must be excluded from the expenses covered by the subsidy before calculating the subsidy

amount and submitting the application.

However, to avoid hindrance to the implementation of the subsidized project, such subsidized project operating entities as those listed below shall be permitted to include the consumption tax in the expenses covered by the subsidy when calculating the amount of subsidy.

- [1] Subsidized project operating entities who are not classified as taxpayers under the Consumption Tax Act
- [2] Subsidized project operating entities who are tax-exempt business entities
- [3] Subsidized project operating entities who are business providers subject to simplified tax
- [4] National or local governments (limited to cases when project is conducted with a special account), or subsidized project operating entities who are corporations listed in the attached Table 3.
- [5] Subsidized project operating entities who are using the general account of a national or local government
- [6] Subsidized project operating entities who are taxable business providers that choose a refund of consumption tax, following confirmation of consumption tax and purchase tax deductions, for instance due to a low amount of taxable sales
- 12. Miscellaneous
 - (1) Any expenses incurred (including expenses for order placement) before the effective date of the grant shall not be covered by the subsidy program.
 - (2) In the event that the subsidized project operating entity desires to make a purchase or other contract related to material procurement or involving an occurrence of cost, it shall invite open competitive bidding, as a general rule, from the viewpoint of cost effectiveness. If the subsidized project operating entity desires to transfer part of the subsidized project to a third party or conduct the project in partnership with a third party, it shall in advance make a contract on the implementation and report this to PMO.
 - (3) Once informed that the decision on grant of the subsidy is made, the subsidized project operating entity shall not change the subsidy budget distribution or the details of the subsidized project nor interrupt or terminate the project without prior approval from PMO.
 - (4) The subsidized project operating entity shall promptly report the progress of the subsidized project and so on whenever required to do so by PMO.
 - (5) After the subsidized project is completed (or the project termination is approved), the subsidized project operating entity shall submit a project result report to the management office.
 - (6) The subsidized project operating entity shall keep accounts on any expenditures for the subsidized project with dedicated account books accompanied by all written evidences in a way that is clearly differentiated from the other accounting to ensure that all incomes and expenditures are meticulously accounted for. The entity shall maintain the account books at least five years after the fiscal year in which the date of completion (or the date of approval for

termination) is included so that they can be accessible whenever requested by METI, fund establishment organization and PMO.

- (7) With respect to the assets acquired or the utility of which has increased through the subsidized project (hereinafter referred to as "the Acquired Assets, etc."), the subsidized project operating entity shall manage them with due care of a prudent manager even after the completion of the subsidized project, and strive to effectively make use of them in accordance with the purpose of the grant of the subsidy. All applicable Acquired Assets, etc. shall be properly controlled using an Acquired Asset Ledger during the asset disposal restriction period, which will be separately set forth.
- (8) If the subsidized project operating entity needs to dispose of (i.e., use, transfer, loan or offer as collateral assets contrary to the purpose of the grant of the subsidy) any Acquired Asset having a unit price equal to or higher than 500 thousand yen (tax excluded) during the asset disposal restriction period separately set forth, they must obtain prior approval. In this case, the entity shall pay part of or the entire subsidy amount as a general rule. (The maximum payment does not exceed the subsidy amount for the appropriate asset to be disposed of).
- (9) After the completion of the subsidized project, the Board of Audit may visit the premises of the subsidized project operating entity for inspection.
- 13. Contact

Toranomon Toyo Bldg. 8th Floor 4-2, Toranomon 1-chome, Minato-ku, Tokyo 105-0001, JAPAN Contact: Mr. Kondo, Mr. Kawai E-mail: hairo-info@ml.mri.co.jp

* Contact us through e-mail. We regret that no inquiries will be accepted via telephone.

(Form 1)

No.	
*Leave blank.	

Management Office for the Project of Decommissioning and Contaminated Water Management

Application for the subsidies for the "Project of Development of Analysis and Estimation Technology for Characterization of Fuel Debris (Development of Technologies for Enhanced Analysis Accuracy and Thermal Behavior Estimation of Fuel Debris)"

Applicant	Corporation number (*)	
	Company/Organization Name	
	Representative (Full Name and Title)	
	Address	
	Contact Person (Full Name)	
Contact	Section/Department	
	Title	
	Telephone (Extension, if any)	
	E-mail	

* If a corporation number in Japan has been given, fill in the 13-digit number.

If you are an individual and foreign company, etc., not having it, leave the field as it is.

(Exhibit)

1. Name of the Subsidized Project

- Objective and contents of the Subsidized Project
 *Describe your own understanding of the background of the project, the purpose of the project and its contents briefly.
- 3. Scheduled commencement and completion dates of the Subsidized Project (Scheduled commencement date):
 (Scheduled completion date):

4. Entire costs needed for the project	JPY
5. Costs subject to subsidy	JPY
6. Subsidy amount to be applied for	JPY

7. Allocation amount of the costs for the Subsidized Project, costs eligible for the subsidy and subsidy amount to be applied for

The contents are the same as (2) Expenditures, I. Summary table of "2. Plan of the income and expenditure of the Subsidized Project" of the Form 2, "Brief explanation of subsidized project".

and expenditure of the Subsidized Project" of the Form 2, "Brief explanation of subsidized project".

- 8. Bases for Calculation for the above amount The contents are the same as (2) Expenditures, II. Distribution of Costs of "2. Plan of the income
- 9. If a group is formed to conduct the Project, the names of the group and the member companies
- Note 1: <u>The "costs required for the Subsidized Project"</u> refers to the cost required for performance of the relevant project. As a general rule, the <u>amount must be provided after deducting the amount of the national and local consumption taxes</u>.
- Note 2: As for the amount of <u>the "Subsidized Costs"</u>, as a general rule, the amount of the "costs required for the Subsidized Project" eligible for the Subsidy <u>must be provided after deducting the amount</u> <u>of the national and local consumption taxes</u>.

Note 3: The "amount of the Subsidy applied for" refers to the amount of the "Subsidized Costs" for which grant of the Subsidy is requested, and the amount limit is the amount of the "Subsidized Costs" multiplied by the Subsidized Ratio (any amount less than JPY1 shall be rounded down).

Remark: The size of the paper used shall be the Japan Industrial Standards A4 Format.

Address

Name (Name of Corporation and Title/Name of Representative Person)

Outline of Subsidized Project

- 1. The implementation plan for the Subsidized Project (based on the period in above "4. Project Term")
 - (1) Contents and implementation method of the project
 - * Provide the following information by project content item.
 - *Specific implementation contents and method, based on clarification of issues for each objective of research and development
 - *Specific implementation content and method for each item of the project content
 - *Specific proposal to improve outcome of the project
 - *Project location (Address and name of the location)
 - (2) The implementation timeline

*Describe the implementation schedule of the project by month for each implementation contents. *Describe the implementation procedure in detail. If the stages of the research and development are different (such as design, development, tests, etc.) in each item, describe the difference clearly. *If the persons in charge of the research and development (manufactures and subcontractors) are different in each item, describe the organization they belong to clearly so that we can distinctly understand who will actually implement the item.

- *Set the actual targets for achievement of the project purpose as milestones and describe them for each item.
- In setting the milestones, they must be related to the points where delay of the project is foreseen.
 In order to prevent delay, alternative options must be described for items with high risk.
- * Describe major output and input information so that correlation with other projects, comprehensive proposals, partial proposals, etc. can be grasped.
- *As a plan of the interim report, describe the outputs which will have been able to be achieved at the time of the report and further plan.
- ***In reporting your progress, show your plan and actual progress in a comprehensible manner. Furthermore, describe the up-to-date situation and further work plan, etc. as a reference.

(3) The project implementation organization

* Provide the implementation organization chart and the number and role of people who are engaged in the project for each item of the project contents (Attachment 1)

* After clarifying the responsible person for entire project implementation, the project leader (exclusively employed for the project) and sub-leaders responsible for each project item, provide their profile, area of expertise and track record of engagement in similar projects..

*Describe outsourcing or commissioning, if planned.

*Describe the name, outline, year, ordering party, etc. of similar projects. If the project was done as your own company's project, state it accordingly.

*Clearly state the experiences of each participating party if you form a consortium.

2. Plan of the income and expenditure of the Subsidized Project (based on the period in above "4. Project Term")

(1) Income	(Unit: JPY)
Item	Amount
Own fund	
*Bond issuance or borrowing	
Other	
Subsidy	
Total	

*Attach the documents to show the funding plan relating to the relevant bond issuance or borrowing.

(2) Expenditures

I. Summary table

(Unit: JPY)

			Classification of the cost burden		
Classification of	Costs required for the Subsidized	Subsidized Costs	The amount of cost borne by the	The amount of the	
costs	Project	Subsidized Costs	Subsidized Project	Subsidy applied for	
			Operating Entity		
Labor Cost					
Operating cost					
Total					

II. Distribution of Costs (provide the details by project item)

*Describe in this sheet or other separate sheets the name of the goods, unit price, man-hour, etc. as basis for the calculation.

***If you form a consortium, clearly describe the breakdown of each company or organization.

(L	Jnit:	JPY)
		U ,

Type (Example)	The cost required for the Subsidized Project	Subsidized costs	Amount of the Subsidy applied for	Remarks
【Labor Cost】				
• • •				
Sub total				
[Operating Cost				
]				
Raw material				
Goods purchase				
Outsourcing				
• • •				
Sub total				
Total				

- (Note 1) The <u>"cost required for the Subsidized Project</u>" refers to the cost required to perform the relevant project. As a general rule, provide <u>the amount after deducting the amount of the national and local</u> <u>consumption taxes</u>.
- (Note 2) As a general rule, provide the "<u>cost required for the Subsidized Project</u>", which is eligible for the <u>Subsidy after deducting the amount of national and local consumption taxes</u> in the "Subsidized Costs".
- (Note 3) The "amount of the Subsidy applied for" refers to the amount of the "Subsidized Costs" for which grant of the Subsidy is requested, and the amount limit is the amount of the "Subsidized Costs" multiplied by the Subsidized Ratio (any amount less than JPY1 shall be rounded down).

Remark: The size of the paper used shall be the Japan Industrial Standards A4 Format.

- 3. Financial basis and management system
 - * Describe the outline of your organization; moreover, describe the grounds on which your organization has necessary management basis for smooth implementation of the project as Annex 2.
 - *Describe the grounds on which your organization is capable of managing funds, etc. (such as organization and storage of evidence documents for expenditures). Furthermore, describe the scheme of the management of the funds (responsible persons and their roles).
 - * If you form a consortium, all of the above-mentioned items must be described regarding every organization.

Implementation Organization Chart

Content of the	• Develop an organization chart to show the framework for implementation of		
descriptions	the Project		
	• The names, titles and division	of roles of the personnel in charge must be	
	contained in the implementation	on organization chart	
	Clarify persons exclusively em	ployed for this project described in this Chart;	
	and describe the career back	round, expertise, area of specialty at work,	
	qualification associated with the	ne project, and other relevant information must	
	be provided about the key personnel.		
Operational Imple	mentation Organization		
*A concrete description	on should be provided by showing a	n implementation organization chart containing	
the following informat	ion for each project item.		
*Specify the name of	the contact person in case of a joint a	application	
\			
• Name			
• Title			
Role in thi	s Project, etc.		
		Member	
		Name	
		Title	
		Role	
Leader	Sub-leader	Qualification	
Name	Name		
Title	Title		
Role	Role		
Qualification	Qualification	Member	
		Name	
		Title	
		Role	
		Qualification	

(Annex 2) Outline of your organization

Note: If you form a team and apply, you must fill in this sheet for every participant.

*Fill in the data of the latest accounting year in non-consolidated base.

Company name									
Title/name of the									
representative									
person									
Contact	Tel:			Fax:					
information	E-mail:	E-mail:							
Head office's									
address									
Date of	Date:	Ac	count		Small- or				
establishment	Dale.	closir	ng month		medium-sized				
	JPY in thousands				company				
					(indicate by a				
		Nhur	nber of		circle if the	\circ or $ imes$			
Capital					company is a				
		Em	oloyees		small- or				
					medium-sized				
					company)				
Description of									
business									
Major	000 (company limited))							
Major shareholders	(60%)								
	$ abla_{\Box \circ}$ (company limited	d)							
(equity	(30%)								
ownership)	□ ○ ○ (company limited)	(1%)							

(The title and name of the person responsible for above information:

Head of the XX Department, XX XX(Name) and his/her signature)

	4 .			41 12.4.1 1
Please provide	the information	about all	officers in	the list below:

	Date of Birth					
Full name in Katakana	Japanese era			Sex	Company Name	Title
Full name in Chinese characters	name	Month	Day	007	Company Name	The
	Year					
(Example) Taro Keizai	S 35	01	01	М	Keizai Sangyo Co., Ltd.	President &
Taro Keizai						Representative
						Director

- (Note 1) Add the columns as appropriate if the provided columns are not sufficient to provide full information.
- (Note 2) Use one-byte characters and put a space between the first and last names to provide the names in Japanese phonetic symbols (katakana).
- (Note 3) Use two-byte characters and put a space between the first and last names to provide the names in Chinese characters.
- (Note 4) The letters T, S, H or R should be used to indicate the Japanese era names for the date of birth and the year should be indicated by a two-digit number.
- (Note 5) Use M for male and F for female in one-byte characters to indicate the sex.
- (Note 6) For a foreign national, use the alphabet characters to indicate the person's full name in the "Full name in Chinese characters" and the pronunciation of the name in Katakana in the "Full name in Katakana" column.
- (Note 7) For a joint application or a Project C, provide the information about all officers of each and every member (company or otherwise) of the group.

(Remarks) The size of the paper used shall be the Japan Industrial Standards A4 Format.

(Other documents)

- (1) Outline of the company or organization such as a brochure, etc.
- (2) The financial results, and statement of revenues and expenses (for the past one year)
- (3) The articles of association or the act of endowment
- (4) Other supporting documents (as needed)

(Form 3)

Certificate of Conformance to Qualification Requirements for the Project of Development of Analysis and Estimation Technology for Characterization of Fuel Debris (Development of Technologies for Enhanced Analysis Accuracy and Thermal Behavior Estimation of Fuel Debris)

I confirm that the applicant satisfies the qualification requirements for this subsidized project.

firm that the applicant satisfies the qualification requirements for	this subsidized project.
Requirements	Verification, etc.
Possessing the organization for properly conducting the relevant subsidized project.	<state applicant="" satisfies="" that="" the="" the<br="">requirements with reasons in detail ><see "1.="" (3)="" 2="" form="" project<br="">Implementation Organization" when necessary."></see></state>
Having the capacity, knowledge and experience required for conducting the relevant subsidized project.	<state applicant="" satisfies="" that="" the="" the<br="">requirements with reasons in detail ><see "1.="" (3)="" 2="" form="" project<br="">Implementation Organization" when necessary."></see></state>
Having the management foundation required for smoothly conducting the relevant subsidized project and sufficient ability to control the funds and other resources.	<state applicant="" satisfies="" that="" the="" the<br="">requirements with reasons in detail ><see "(3)="" 2="" basis<br="" financial="" form="">and management system when necessary."></see></state>
Being able to implement the project in accordance with all the applicable laws and regulations enacted in Japan, and to follow the appropriate accounting procedures in accordance with "Grant Policy for Subsidy for the Project of Decommissioning and Contaminated Water Management" and "Subsidized Project Administration Manual". https://en.dccc-program.jp/files/20190405man.pdf	<state left="" on="" statement="" that="" the="" understand="" you=""></state>
Not foreseen to be subject to Articles 70 and 71 of the Cabinet Order concerning the Budget, Auditing and Accounting.	<pre><state applicant="" apply="" does="" it="" not="" that="" the="" to=""></state></pre>
Not fulfilling any of the conditions stipulated in the "Guidelines for the suspension of subsidies controlled by the Ministry of Economy, Trade and Industry and the suspension of designation relating to the contracts". (January 29, 2003, No 1) First column, the second items in Attachment	<pre><state apply="" does="" it="" not="" that="" the<br="" to="">applicant></state></pre>
Research and development companies which may require approval under the Foreign Exchange Act for any exports and imports should have an establishment of internal compliance program(ICP) under a self-control system about the "standards for exporters, etc. to meet" provided for in Article 55-10 (1) of the Foreign Exchange and Foreign Trade Act.	<describe condition="" form="" in="" meeting="" no.5="" the="" this=""></describe>
Admitting that the results obtained through this project can be utilized by TEPCO Holdings, Incorporated, etc. to leverage them for Decommissioning and Contaminated Water Countermeasures if they request to do so under the condition that each party is in agreement. Not preventing the utilization by behaviors such as not admitting use of the technology intentionally, asking for unreasonable compensation, etc. in spite of receiving the request.	<state is="" it="" possible="" that=""></state>
t t i	hem for Decommissioning and Contaminated Water Countermeasures if they request to do so under the condition hat each party is in agreement. Not preventing the utilization by behaviors such as not admitting use of the technology intentionally, asking for unreasonable compensation, etc. in

water management at the Fukushima Daiichi NPS by ceding the above-mentioned condition in (8) to the successor if the applicant hands over the result to a third party and loses their own right to utilize it accordingly. In the case of a conflict which makes the applicant unable to make sure of the items in (8), the concerned parties must solve it by their own responsibility.

<Note for Filling out this Form>

In the verification columns, please write the reasons why you verified that the applicant meets the requirements. When filling it out, write "Attachment" if there are any verification documents attached to this form and if not, write "No attachment."

(Form 4)

Input/Output information on Project of Development of Analysis and Estimation Technology for Characterization of Fuel Debris (Development of Technologies for Enhanced Analysis Accuracy and Thermal Behavior Estimation of Fuel Debris)

* Please refer to the reference document 1 as an example.

ID	Requested projects	Offered projects	Contents (outline)	Time when the project is necessary	How to use the information	Remarks
						Such as measures
						for the case when
				*Influences of delay		you cannot ensure
				(if any)		the accuracy, cannot
						keep the timeline,
						etc.

(Form 5)

Response to Security Export Controls on Project of Development of Analysis and Estimation Technology for Characterization of Fuel Debris (Development of Technologies for Enhanced Analysis Accuracy and Thermal Behavior Estimation of Fuel Debris)

Response to Security Export Controls								
Circle one of the following three options: handled, not handled or not required.								
Handled	Submit relevant documents (export control regulations for security trade)							
	State the date of submission: Year Month:							
Not handled	State future plans							
	State reasons							
Not								
required								

```
(Form6)
```

Personal Data Processing Consent Form

Purposes

In compliance with the Act on the Protection of Personal Information, Mitsubishi Research Institute, Inc.("MRI") requests your consent to use your personal data to evaluate of proposal.

Data Sharing

MRI may share your personal data with cooperating organizations.

Data Retaining

There are cases in which it is necessary to retain your personal data for the necessary period according to the requirements of Japanese law.

Data Management

MRI will protect your personal data securely, including taking necessary measures to prevent leakage, loss, falsification, etc.

I have understood the above and give my consent to MRI to use my personal data for the							
above Purposes, and to carry out the above Data Sharing and Data Retaining.							
Your Full name							
Your Signature							
Date							

If you wish to modify your personal data or withdraw this consent after submission, please notify us by email to privacy@mri.co.jp.

Mitsubishi Research Institute, Inc. 10-3, Nagata cho 2-chome, Chiyoda-ku, Tokyo, Japan +81-3-6705-6004, <u>privacy@mri.co.jp</u>

PMS05_20180718

(Reference Document 1)

ID	Requested projects	Offered projects	Contents (outline)	Time when the project is necessary	How to use the information	Remarks
1_1	Development of investigation technology for inside the nuclear reactor pressure vessels	Development of fuel debris criticality control technology	Needs for sampling of fuel debris	December 2015	Examination of possibility of fuel debris sampling technology	
1_2						
1_3						
1_4	:	:	:	:	:	:

(Reference Document 2)

			Fis	calYe	ear 20)1X						Fis	cal Ye	ear 20)1Y					Remarks
ltem	Item Sub item		Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	O ct	Nov	Dec	Jan	Feb	Mar	(Up-to-date situation)
	(1) Survey of on-site situation and relevant technologies				Compil	ation 7	Desi	gn com	pleted			ogress tem	of each			Descri	be mon	thly lev	el	0000
	(2) Machinery design								P	roducti	on com	pleted								0000
Validation	(3)Machinery production			De	sign co	mpleteo	1										Des		up-to-da vork scl	ate situation and hedule
Validation on XX	(4) Establishment of tests plan			ſ							<u> </u>	i-site in	stallatio	n	т	est con	npletion			0000
	(5) Tests implementation	Describe milestones in each item (related to high-risk points)						,	Result of machinery											
	1 Y Z		e project item, (r		_												development			
	(7) Compilation of results		d clarify and sta		-	entity							Des	cribe r	najor ir	n-put/ou	ut-put			
Validation on XX	(1) YY													Describe the available results foreseen at interim report			interim report			
(when alternative s are	Describe items for which needed.	alterna	tives ar	re										and further plan						
needed)														L	_					
			Cor	npletior	of pla	n estab	lishmer			demor	enceme istration					ompleti				
Major miles	tones							Interin	n repor	t			Interim	report	den	nonstra	tion test		Results	report

Table 1 Example of implementation schedule with points of attention

(Reference document 3)

Regarding Subsidized Cost Items

Regarding the cost items defined in "The Decommissioning and Contaminated Water Management Project Implementation Guidelines", please refer to the following table.

Cost item	Description	Correspondence with "Subsidized Project Administration Manual"					
I. Labor cost	abor cost for working hours of those engaged in the project. 3. Accounting process on labor cost						
II. Operating cost							
Raw material cost	Expenses necessary for purchasing raw material or material necessary for implementing the project %Here, "raw material" denotes what loses its nature and is used for production or manufacturing of entirely new ones; "material" denotes what does not lose its nature and is a constituent element of produced items or manufactured items only through being put to new application.	7. Accounting procedures regarding supplies expenses					
Supplies expense	Cost for the purchase of goods necessary for performing the project but not belonging to raw material cost (however, only those verifiable for the use in the project)	7. Accounting procedures regarding supplies expenses					
Design, production and processing costs	The thing which the subsidized entity cannot design, produce or process, or the cost necessary for outsourcing what is appropriate and does not belong to Facility and equipment cost to other entity. (contract for work)	8. Accounting procedures regarding outsourcing expenses					
Facility and equipment cost	Cost necessary for purchasing, production or installation of facility or equipment necessary for undergoing the project %The actual contents of the "facility and equipment" shall be "buildings and accompanying facilities", "structures" and "machinery and equipment" stipulated in "Ministerial Order regarding depreciable life of depreciable assets, etc." (Fifteenth Order of Ministry of Finance, 1965).	 6. Accounting procedures regarding equipment expenses and rental and hire fees 8. Accounting procedures regarding outsourcing expenses 					
Procurement cost	Cost for the thing which is necessary for undertaking the project and does not belong to facility and equipment cost (at the same time, can be usable more than one year)	6. Accounting procedures regarding equipment expenses and rental and hire fees					
Survey cost	The cost for outsourcing to another entity what the subsidized entity cannot survey or analyze by itself or is not suitable to be conducted by the subsidized entity itself (contract for work)	8. Accounting procedures regarding outsourcing expenses					

Outsourcing	Cost for outsourcing to other business operator what	8. Accounting
cost	subsidized company cannot implement on its own or not	procedures
	appropriate to do so and does not belong to design, production	regarding
	and processing costs, facility and equipment cost or survey	outsourcing
	cost (contract for work)	expenses
Travel	Cost for domestic business travels and overseas business	4. Accounting
expenses	travels necessary for performing the project.	process for travel
		expenses
Gratuities	Gratuities necessary for performing the project (gratuities for	5. Accounting
	external experts who attended meetings, seminars,	process for meeting
	symposiums, etc., gratuities for giving seminars, writing of	expense and
	drafts, cooperation with research, etc.)	rewards
Rent and	Cost for lease and rental of machinery, equipment and the like	6. Accounting
hire	necessary for performing the project	procedures
		regarding equipment
		expenses and rental
		and hire
		fees
Other	Cost for other expenses necessary for undertaking the project	11. Accounting
expenses	which does not belong to any other items	procedures
necessary	Examples	regarding other
for	Commission fee: the cost for outsourcing to other entities of	miscellaneous
undertaking	the cost for assistant personnel or of the cost for temporary	expenses
the project	staffing, which cannot be done or what is not appropriate to be	12. Accounting
. ,	done by the subsidized entity	procedures
		regarding expenses
		for commission
		10. Accounting
		procedures
		regarding assistant
		labor costs, etc.
	1	
